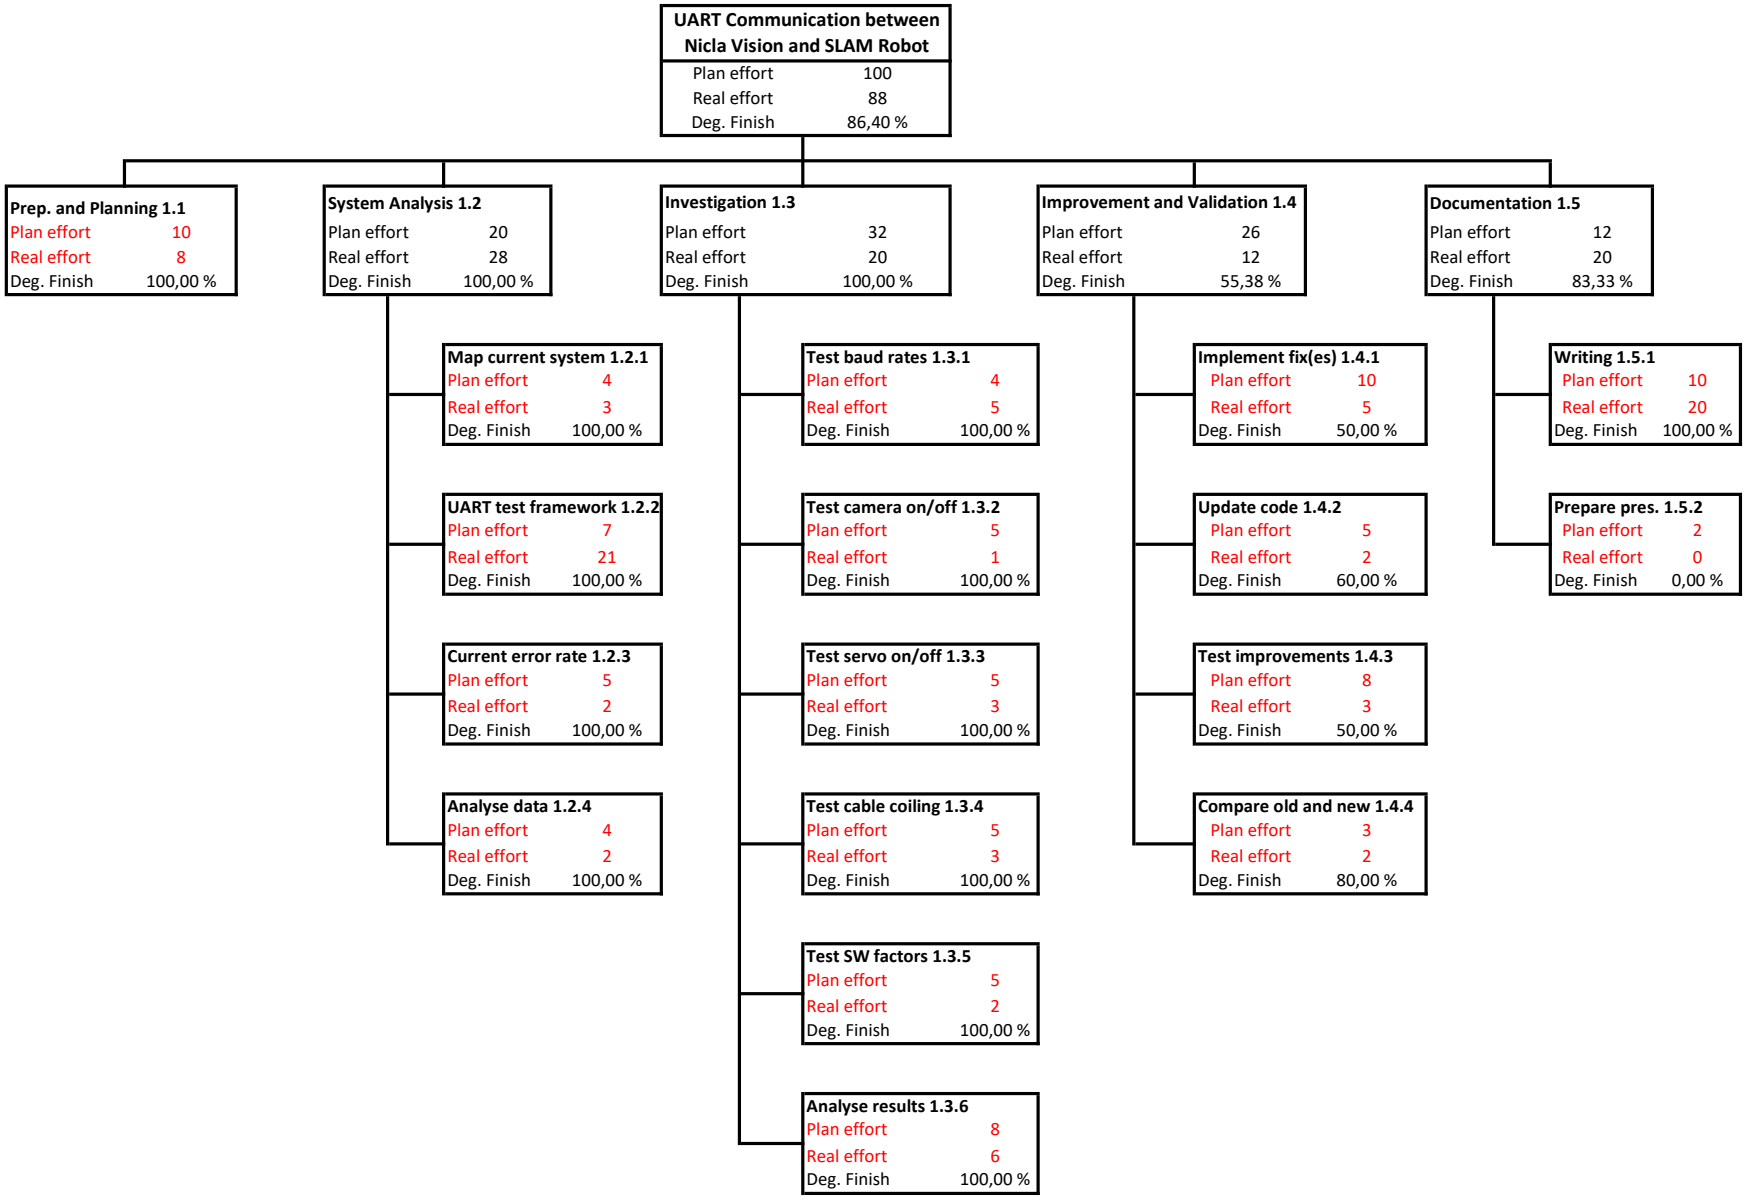

UART Communication between Nicla Vision and SLAM Robot
Plan effort 100
Real effort 88
Deg. Finish 86,40 %
Prep. and Planning 1.1
Plan effort 10
Real effort 8
Deg. Finish 100,00 %
System Analysis 1.2
Plan effort 20
Real effort 28
Deg. Finish 100,00 %
Investigation 1.3
Plan effort 32
Real effort 20
Deg. Finish 100,00 %
Improvement and Validation 1.4
Plan effort 26
Real effort 12
Deg. Finish 55,38 %
Documentation 1.5
Plan effort 12
Real effort 20
Deg. Finish 83,33 %
Map current system 1.2.1
Plan effort 4
Real effort 3
Deg. Finish 100,00 %
UART test framework 1.2.2
Plan effort 7
Real effort 21
Deg. Finish 100,00 %
Current error rate 1.2.3
Plan effort 5
Real effort 2
Deg. Finish 100,00 %
Analyse data 1.2.4
Plan effort 4
Real effort 2
Deg. Finish 100,00 %
Test baud rates 1.3.1
Plan effort 4
Real effort 5
Deg. Finish 100,00 %
Test camera on/off 1.3.2
Plan effort 5
Real effort 1
Deg. Finish 100,00 %
Test servo on/off 1.3.3
Plan effort 5
Real effort 3
Deg. Finish 100,00 %
Test cable coiling 1.3.4
Plan effort 5
Real effort 3
Deg. Finish 100,00 %
Test SW factors 1.3.5
Plan effort 5
Real effort 2
Deg. Finish 100,00 %
Analyse results 1.3.6
Plan effort 8
Real effort 6
Deg. Finish 100,00 %
Implement fix(es) 1.4.1
Plan effort 10
Real effort 5
Deg. Finish 50,00 %
Update code 1.4.2
Plan effort 5
Real effort 2
Deg. Finish 60,00 %
Test improvements 1.4.3
Plan effort 8
Real effort 3
Deg. Finish 50,00 %
Compare old and new 1.4.4
Plan effort 3
Real effort 2
Deg. Finish 80,00 %
Writing 1.5.1
Plan effort 10
Real effort 20
Deg. Finish 100,00 %
Prepare pres. 1.5.2
Plan effort 2
Real effort 0
Deg. Finish 0,00 %

Plan of Progress

UART Communication between Nicla Vision and SLAM Robot

					Update 24/9						Update 15/10				Update 29/10				Frist 1 /11						
		7/9 - 13/9		14/9 - 20/9		21/9 - 27/9		28/9 - 4/10		5/10 - 11/10		12/10 - 18/10		19/10 - 25/10		26/10 - 1/11		2/11 - 8/11		9/11 - 15/11		16/11 - 22/11		23/11 - 29/11	
		37		38		39		40		41		42		43		44		45		46		47		48	
Preparation and Planning	10				5	5																			
System Analysis: Map current system	4						4																		
System Analysis: UART test framework	7						1	6																	
System Analysis: Current error rate	5								5																
System Analysis: Analyse data	4									4															
Investigation: Test baud rates	4									4															
Investigation: Test camera on/off	5										5														
Investigation: Test servo on/off	5										5														
Investigation: Test cable coiling	5											5													
Investigation: Test SW factors	5											1	4												
Investigation: Analyse results	8												3	5											
Improvment and Validation: Implement fix(es)	10													2	6	2									
Improvment and Validation: Update code	5															5									
Improvment and Validation: Test improvements	8																8								
Improvment and Validation: Compare old and new	3																	3							
Documentation: Writing	10																	3	6	1					
Documentation: Prepare presentation	2																					2			
		100	0	0	0	5	5	5	6	5	8	10	6	7	7	6	7	8	6	6	1	0	2	0	0	0	100
